


BIG RIVER COALITION

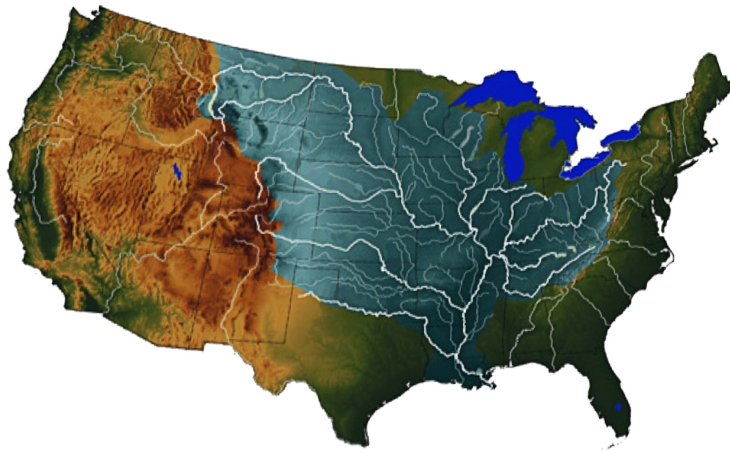

Sean M. Duffy, Sr.
Executive Director
4741 Utica Street, Suite 200
Metairie, LA 70006

Direct Line: (504) 338-3165
Fax Number: (888) 254-4553

sean.duffy@bigrivercoalition.org

June 30, 2021

LOWER MISSISSIPPI RIVER (LMR) DREDGING UPDATE 63021

Members,

The U.S. Army Corps of Engineers (USACE) completed the Phase 1 dredging for the historic project to deepen the Mississippi River Ship Channel (MRSC) to 50 feet on May 7, 2021. The Phase 1 section of the Ship Channel extends from Venice at Mile 13 Above Head of Passes (AHP) to Mile 22 Below Head of Passes (BHP). The USACE uncovered some depth anomalies with two utility pipelines and one cable that cross under the Ship Channel in the area of Venice from Mile 12 AHP to Mile 11 AHP. Due to the information uncovered the USACE is working to verify the depth over these structures in this area before the Ship Channel is officially opened up to a deepened draft (50 Feet). The USACE has actively worked to define the extent of this problem by identifying and contacting the listed utility owners and is awaiting updated surveys and operational information for each potential obstruction. **The USACE is working to maintain or restore at least half of the authorized channel width or the central 250 feet of the channel on the Crossings. (Federally authorized channel dimensions remain 45 feet deep by 500 feet wide.)**

DUSTPAN DREDGES WORKING ON THE CROSSINGS ABOVE NEW ORLEANS:

HURLEY: The government dustpan dredge HURLEY continues dredging the central 250 feet of channel at Red Eye Crossing (Mile 224 AHP). The HURLEY commenced dredging on the Crossings on Wednesday, May 26, 2021.

WALLACE McGEORGE: The industry dustpan dredge WALLACE McGEORGE continues dredging the central 250 feet of channel at Sardine Point (Mile 219 AHP). The dustpan dredge began dredging on the Crossings on May 20, 2021.

JADWIN: The government dustpan dredge commenced dredging the central 250 feet at Philadelphia Crossing (Mile 183 AHP) earlier today. The JADWIN's next assignment will be a quick one at Alhambra Crossing (Mile 190.5 AHP) with no restrictions expected for the White Castle Anchorage. The dustpan dredge is scheduled to head to a shipyard for repairs but is expected to resume dredging on the Crossings in late July. The JADWIN started dredging on the Crossings on June 24, 2021.

BIG RIVER COALITION

INDUSTRY HOPPER DREDGES WORKING IN THE AREA OF SOUTHWEST PASS (SWP):

NEWPORT: The industry hopper dredge NEWPORT (Manson Construction) continues dredging in the area of the Head of Passes from Mile 2.0 AHP to Mile 1.0 BHP under Southwest Pass Hopper Dredge Rental Contract #7-2020. This contract was awarded to the Manson Construction in Fiscal Year 2020 to perform channel maintenance in Fiscal Year 2021. The NEWPORT began work under this contract on April 3, 2021.

CUTTERHEAD DREDGE(S) IN THE HOPPER DREDGE DISPOSAL AREA (HDDA):

ILLINOIS: The cutterhead dredge ILLINOIS (Great Lakes Dredge and Dock) has removed and beneficially used approximately 8.0 million cubic yards (mcy) of material from the HDDA under Hopper Dredge Disposal Area Cutterhead Rental Contract #1-2019. The contract includes the removal of 10 mcy in the base with options to add an additional 4 mcy. The project is expected to be completed by early 2022. The material is beneficially being used in the West Bay Receiving Area through a submerged dredge pipeline that will have to be removed up completion of the project. The pipeline retrieval will require at least one complete closure on the Ship Channel in the immediate vicinity of the submerged pipeline (Mile 2.0 AHP to Mile 0 – the Head of Passes).

MISSISSIPPI RIVER SHIP CHANNEL DEEPENING PHASE 1:

The Phase 1 areas of the Ship Channel have all been deepened to 50 feet through the use of the four dredges listed below. The USACE utilized three contracts to deepen the Ship Channel from Venice to the Gulf of Mexico (Phase 1). The USACE expects to complete the deepening project in four progressive upriver phases to the upper end of the MRSC at Mile 233.8 AHP (Baton Rouge). The details on the dredge contracts worked under Phase 1 of the historic river deepening project are detailed below:

Southwest Pass Cutterhead Dredge Rental Contract #1-2020: was awarded to Weeks Marine on August 20, 2020. This contract was completed by the cutterhead dredges CAPTAIN FRANK that dredged from September 11, 2020 until March 3, 2021 and the E.W. ELLEFSEN that dredged from November 18, 2020 until March 19, 2021.

Southwest Pass Cutterhead Dredge Rental Contract #2-2020: was awarded to Manson Construction on August 27, 2020. The cutterhead dredge ROBERT M. WHITE dredged under this contract from October 23, 2020 until completion on March 18, 2021.

Southwest Pass Hopper Dredge Rental Contract #9-2020: was awarded to Manson Construction on September 21, 2020. The GLENN EDWARDS worked under this deepening contract from January 14, 2021 until completion on May 7, 2021.

Sincerely,
Sean M. Duffy, Sr.

Sean M. Duffy, Sr.
Executive Director

Attachments
